



Areas of Operable Unit 5 (The River and Portage Creek)

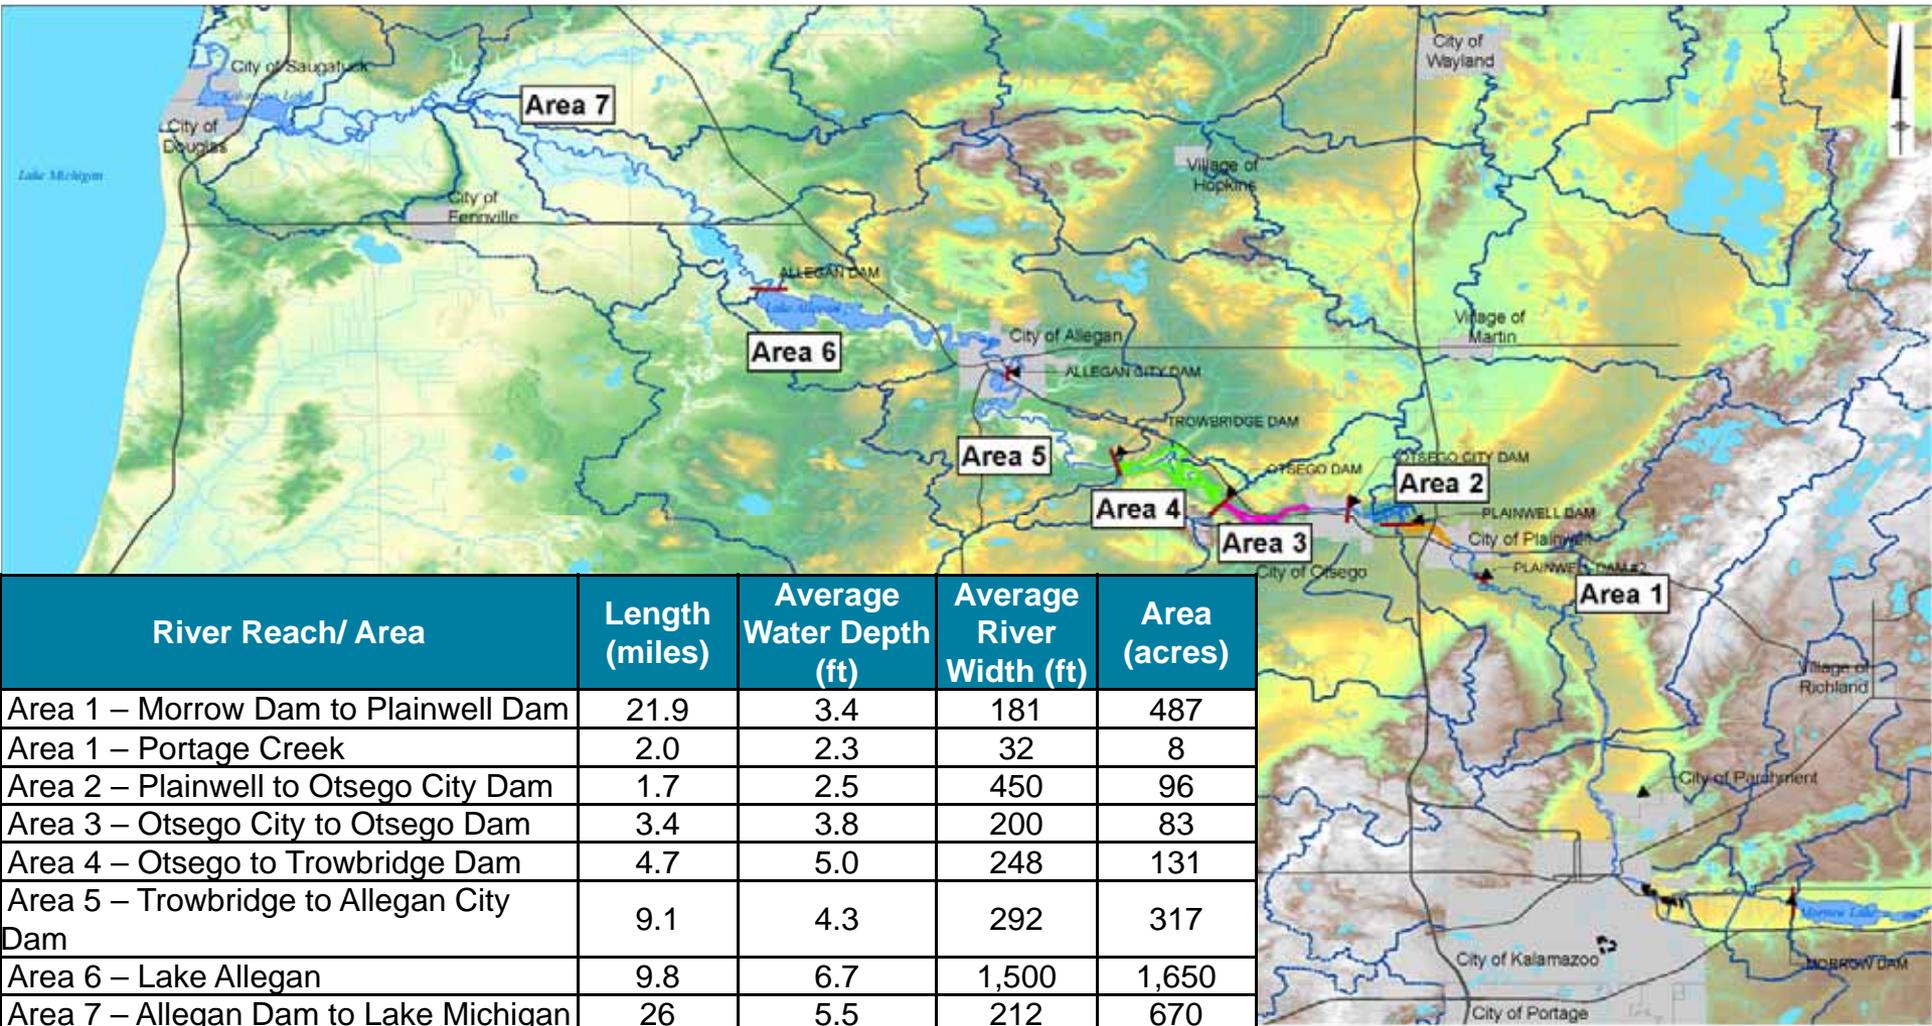

Area 1 – Morrow Dam to Plainwell Dam, Lower Reach of Portage Creek

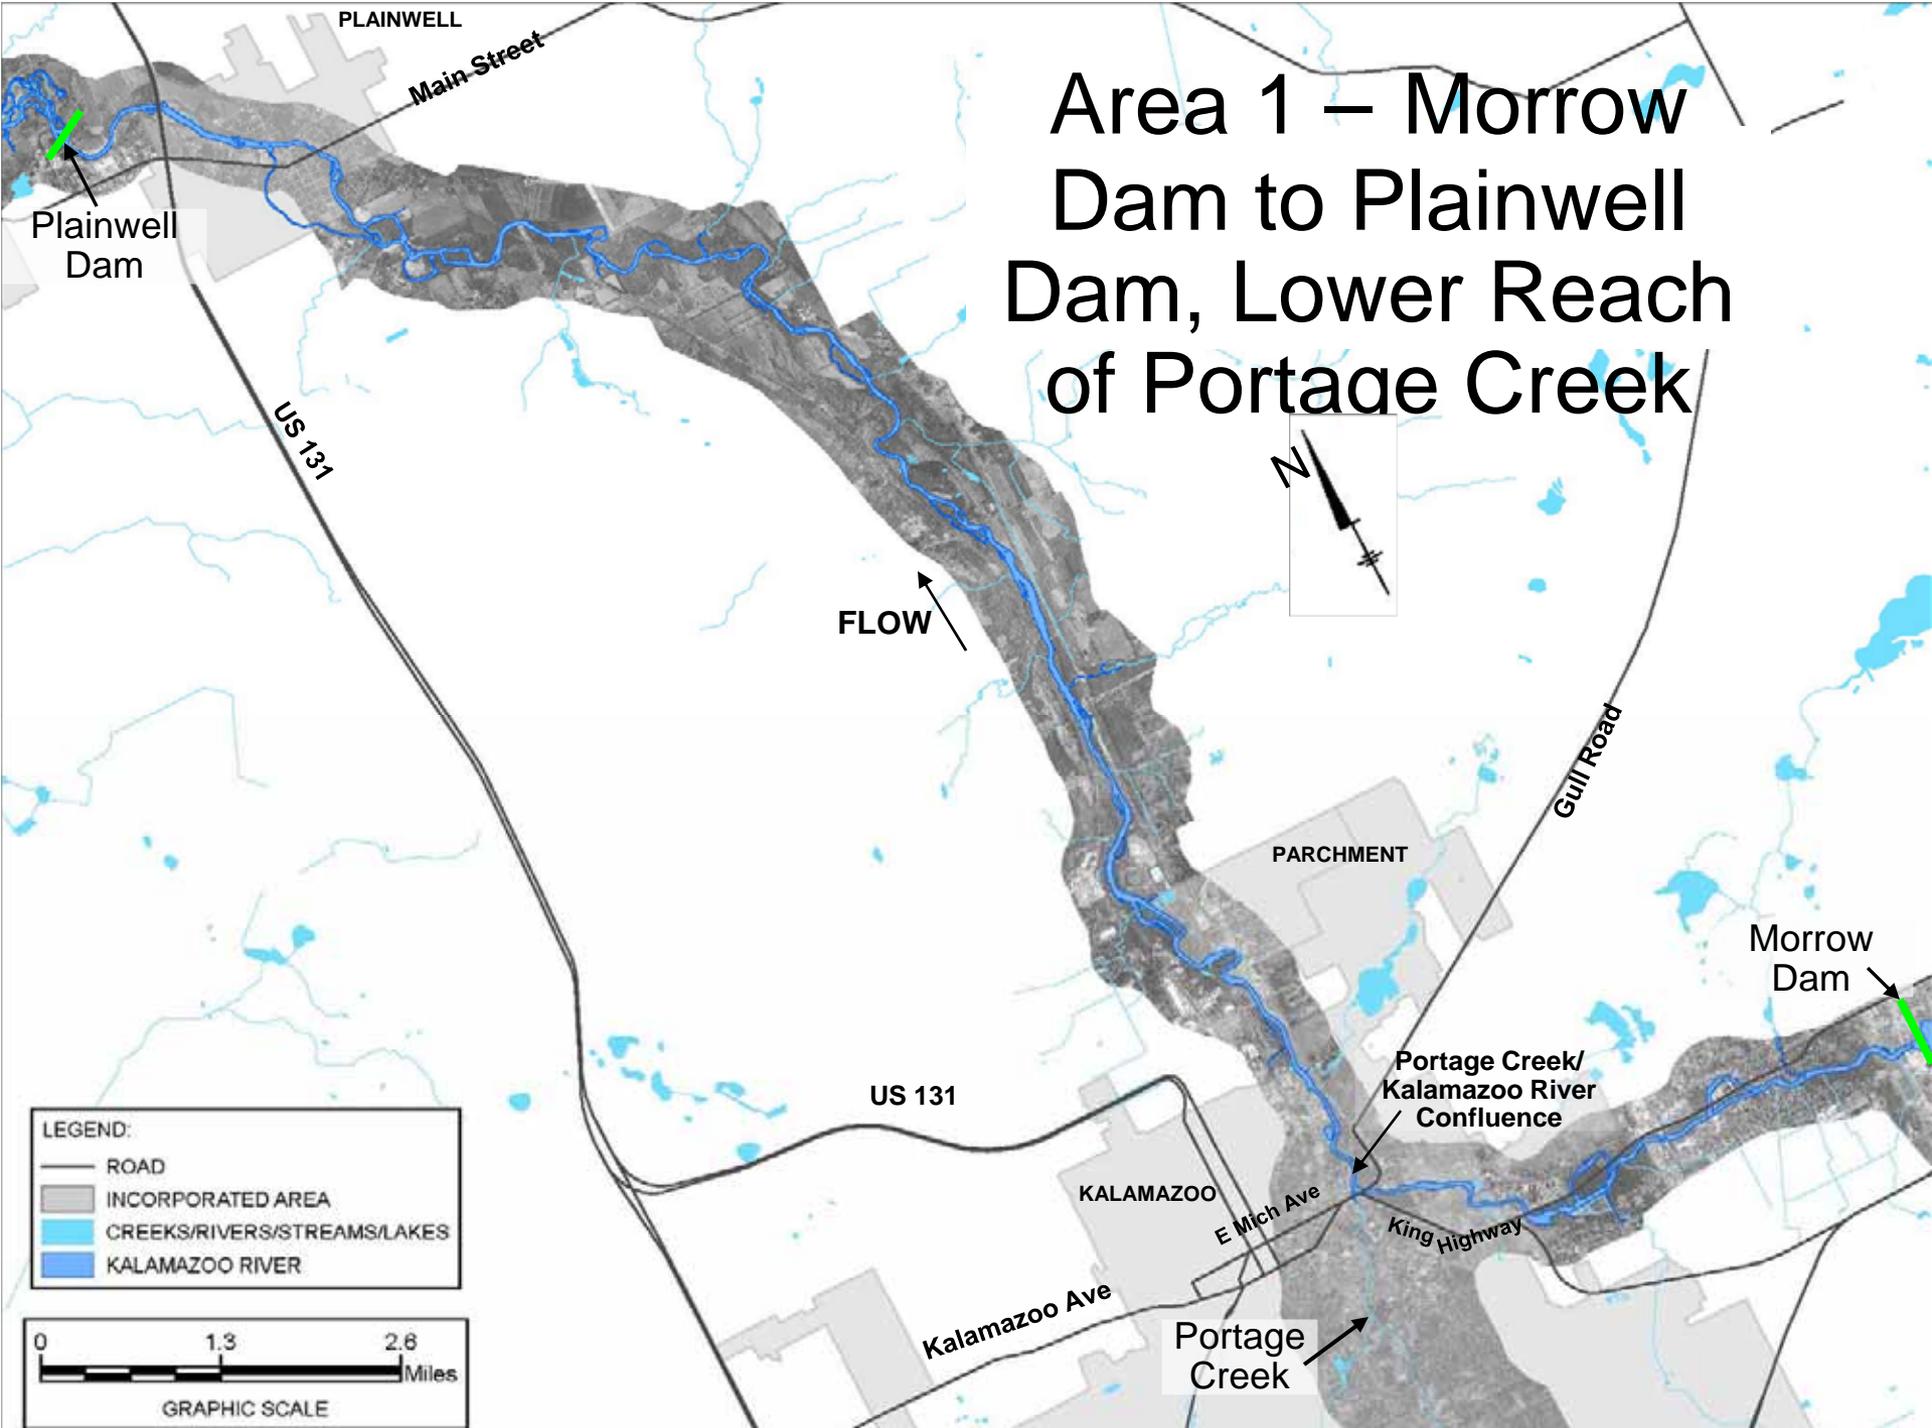


Update on River Progress

AREA 1

- Supplemental Remedial Investigation/Feasibility Study (RI/FS): Draft submitted 4/22/11 to EPA
- Feasibility Study of potential remedial alternatives to be submitted in Fall/Winter 2011
- Final remedy decision for Area 1 in late 2012

AREA 2: Otsego City Impoundment

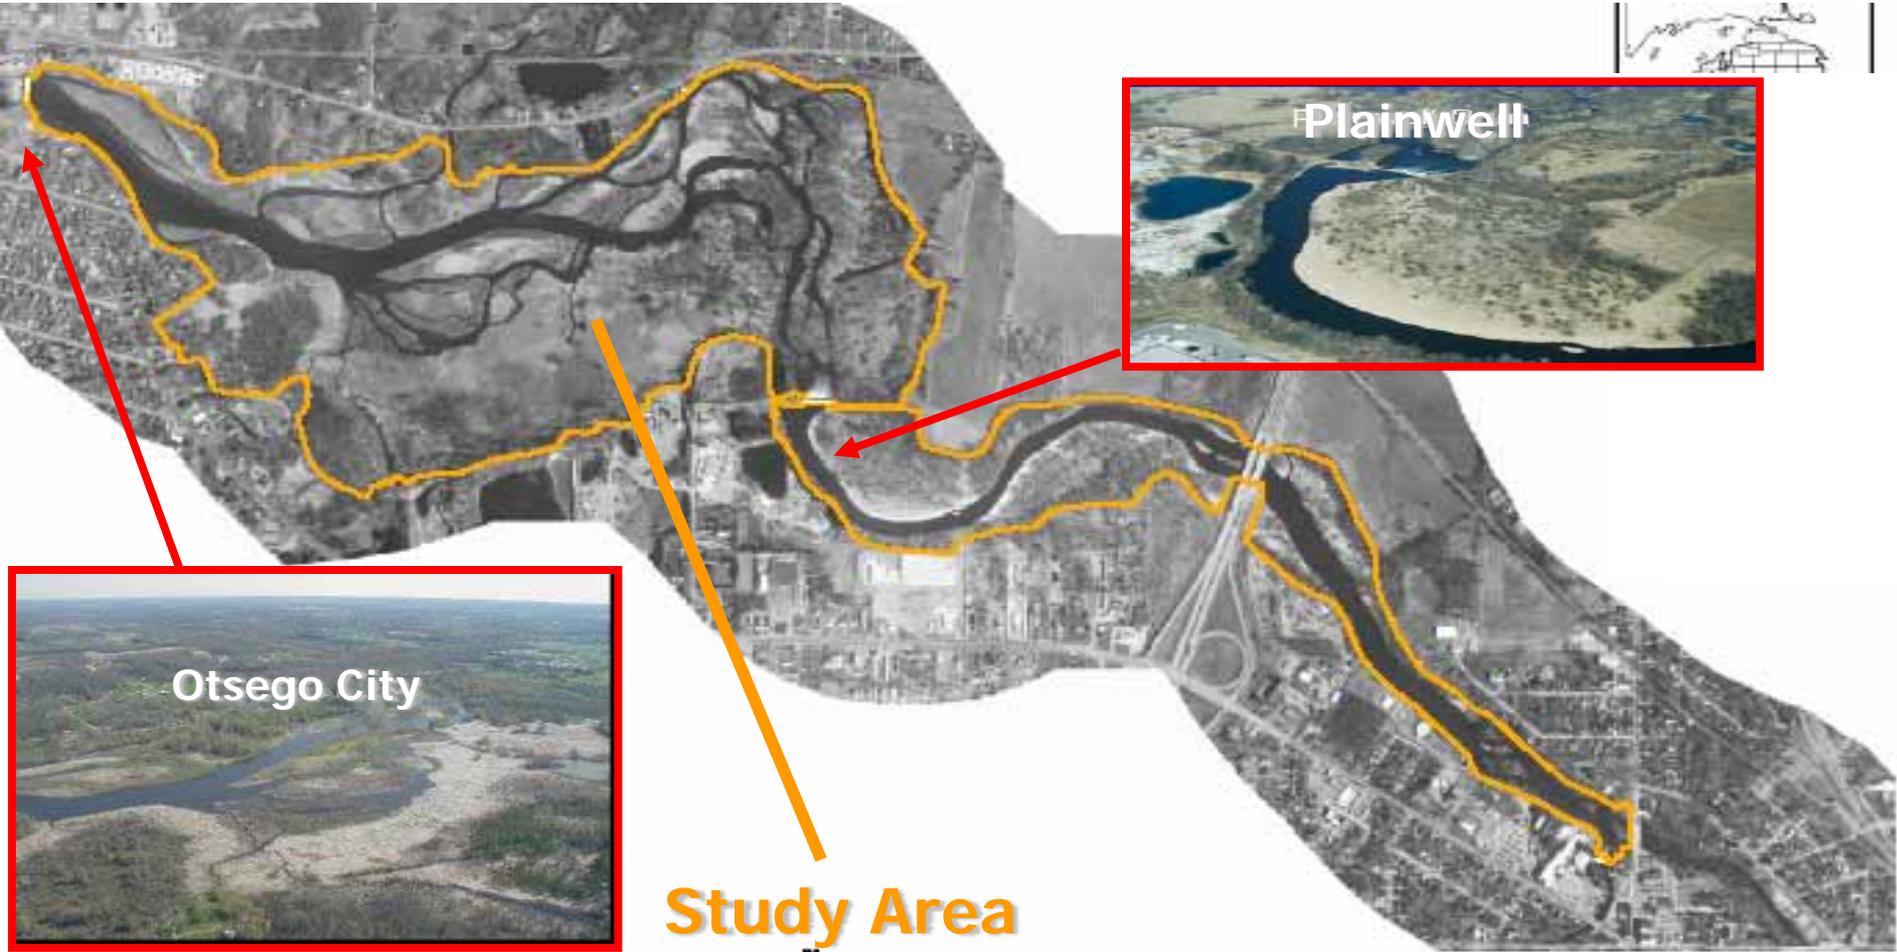

Legend
Floodplain Soil Study Area



DRAFT
Figure 3-1
Floodplain Soil Study Area
Kalamazoo River
Plainwell and Otsego City Impoundments

Update on River Progress

AREA 2


- Conducting field reconnaissance Winter/Spring
- Supplemental RI/FS sampling to begin Summer through Fall 2011
- Two field seasons to complete RI/FS investigation

Update on River Progress

AREA 3


- September 1, 2011: Start of Area 3 Supplemental RI/FS
- Field work to begin in Spring 2012

Plainwell No. 2 Dam Area

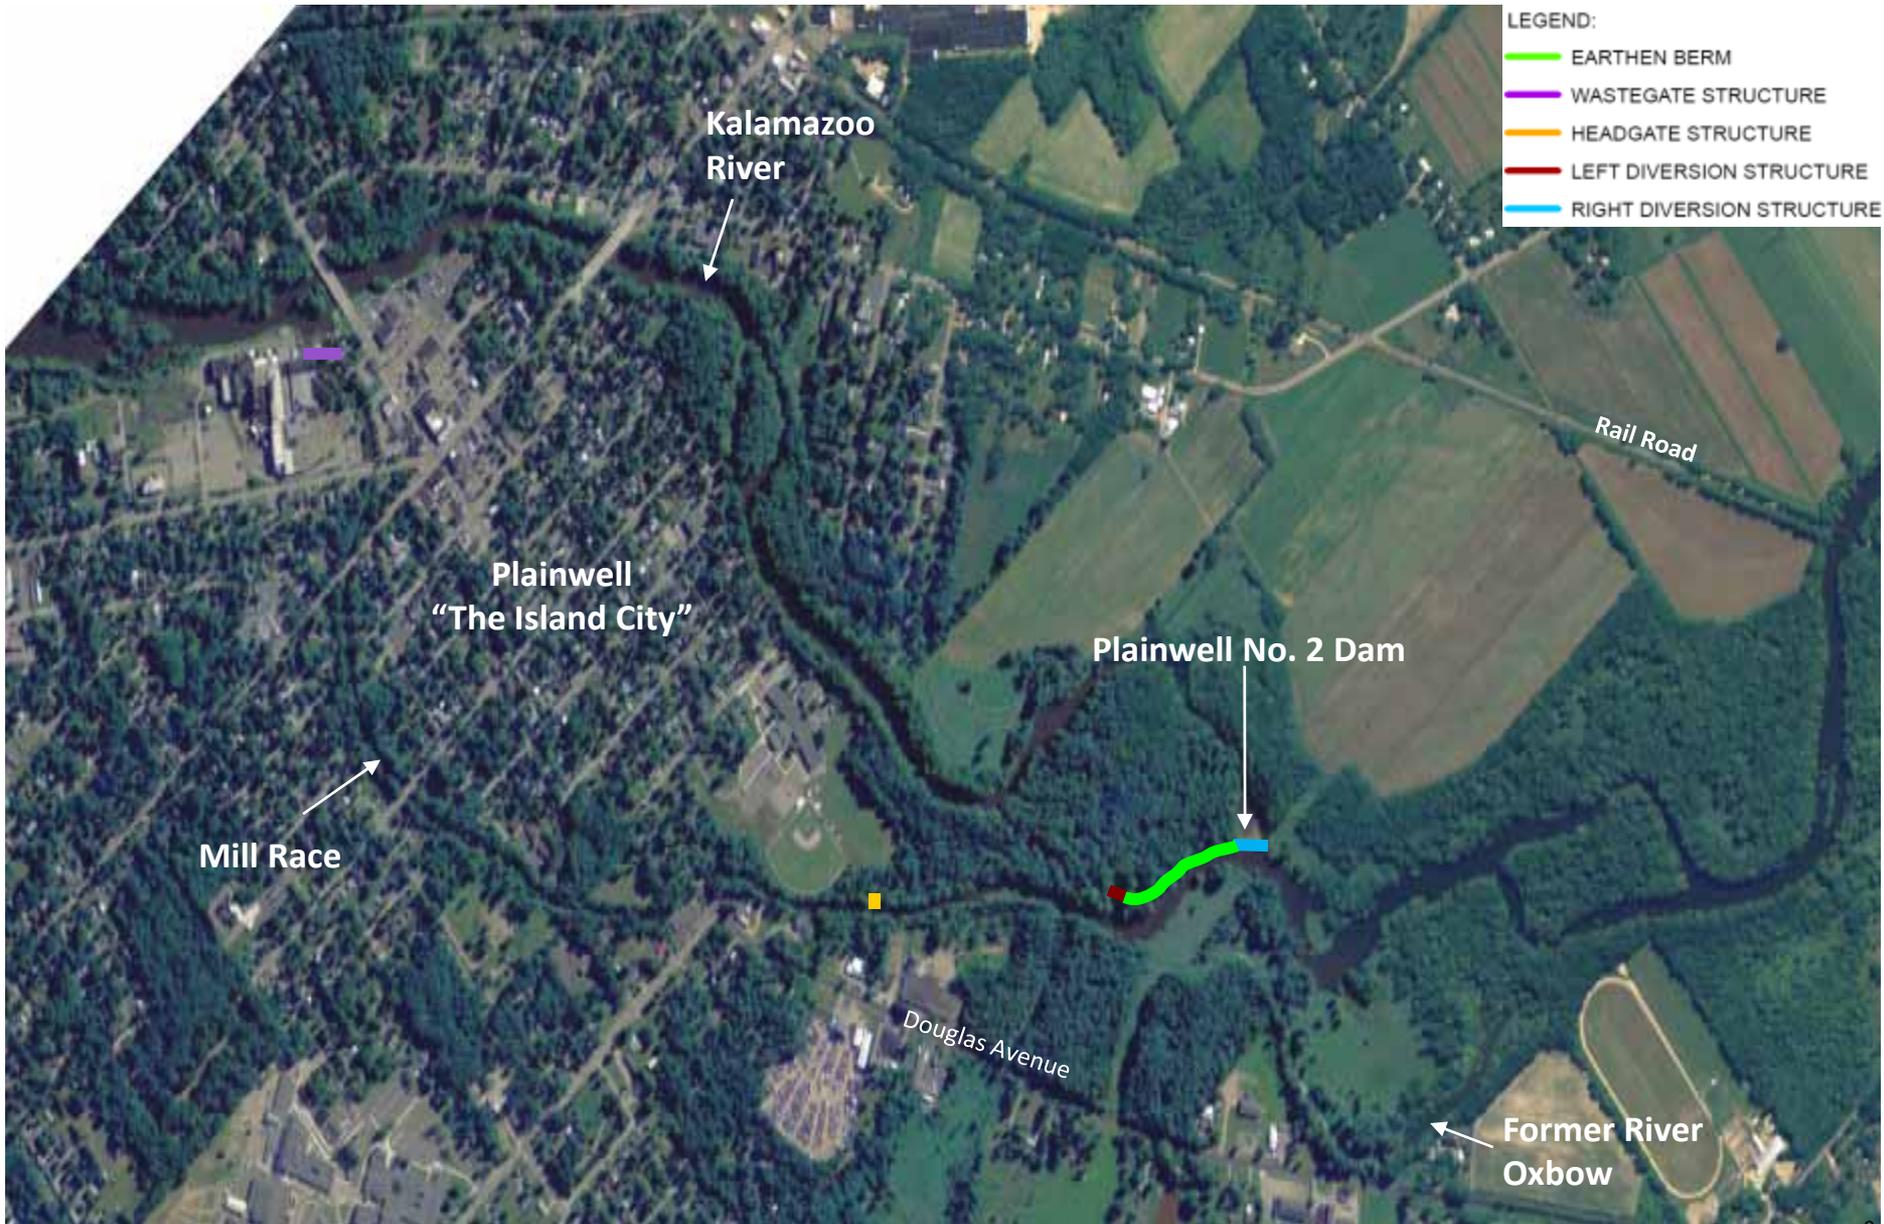

Plainwell No. 2 Dam Area

Time-Critical Removal Action Project Area: 2009-2010

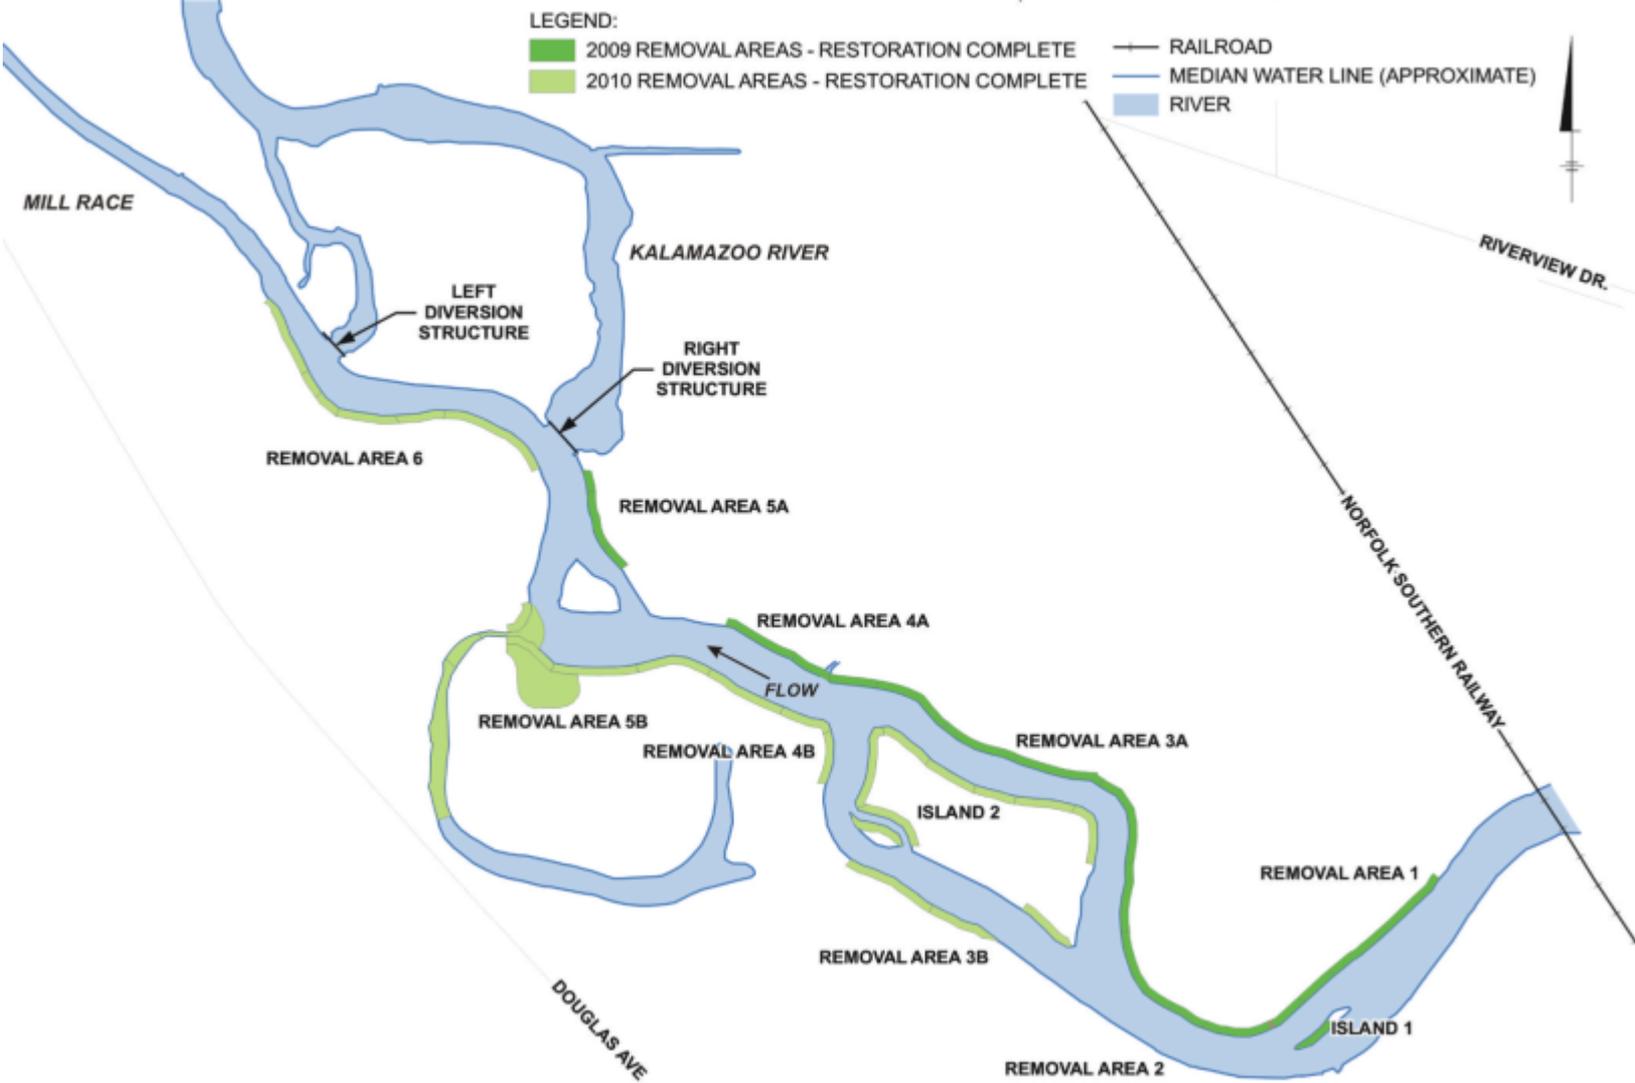

Plainwell No. 2 Dam

PROJECT ACTIVITIES

- Access to River
- Construct staging areas and roadways
- Excavation, Verification and Restoration
- Habitat Restoration and monitoring – 3 yrs
- Bank Monitoring – 3 yrs
- Vegetation Monitoring – 3 yrs
- Exotic/Invasive Species Control

Summary of Construction Activities

	2009	2010	Total
Bank Length Removed (linear feet)	4,300	6,700	11,000
Volume Removed (cubic yards)	5,000	13,500	18,500
Material Disposed (tons)	7,700	16,200	23,900
Area Restored (acres)	6	5	11
Woody Plantings (trees and shrubs)	1,120	1,984	3,104
Confirmation Samples Collected	396	984	1,380

